CONTAINER ONE containerone.net × Autonomous

PHP → Django Migration

Replace fragile PHP infrastructure with a maintainable Django middleware layer — clean models, automated scheduling, and estimated savings of up to 60–70% on API costs.

YOUR INVESTMENT

$22,300 USD

PREPARED FOR	PREPARED BY	DATE	VALID FOR
Container One	Autonomous Technology Inc.	March 19, 2026	30 Days

YOUR SITUATION

Critical audit findings — March 2026

40+	~$4K/mo	5	14–16	617 → 1
PHP FILES → 1 CLEAN APP	API WASTE — FIXABLE	MIGRATION PHASES	WEEKS TO COMPLETION	ADD-TO-CART VS. CHECKOUT EVENTS

Security Vulnerabilities CRITICAL

- `adminer.php` publicly accessible — full DB admin exposed
- `phpinfo.php` public — leaks server configuration
- 30+ SQL injection vulnerabilities across the query layer
- All credentials stored in a single plain-text config file
- PHP display_errors on in production — exposes queries & stack traces
- CORS wide open (`Access-Control-Allow-Origin: *`)

Broken Scheduling CRITICAL

- No cron jobs on server — syncs triggered by external HTTP calls only
- No external caller = pricing updates simply don't run
- `sync-products.php` processes one job per call, no automation
- `cron_and_webhooks` kill switch in DB causes silent failures
- Pricing for 300+ depots can go stale with zero indication

Checkout Tracking Broken HIGH

- Custom `checkout.php` bypasses Shopify's tracking entirely
- 617 add-to-carts recorded, only 1 "begin checkout" event in GA4
- Conversion data is effectively useless for optimization
- No attribution, no funnel visibility, no abandoned cart recovery

Silent Failures & No Observability HIGH

- Container product syncs fail without any log or alert
- No monitoring, error reporting, or alerting of any kind
- Shopify sync queue can back up invisibly for days
- No tests — unknown what "working" even looks like

No Version Control or Staging HIGH

- All deployments done via SFTP file upload
- No staging environment — production is the test environment
- No rollback — a bad deploy is permanent until manually fixed

Method CRM SOAP Integration

- 15 files of legacy SOAP XML via `nusoap`
- Method CRM being phased out — all this code is dead weight
- Tightly coupled — can't be removed incrementally without risk
- Django migration removes all 15 files cleanly in Phase 4

PHP today — the chaos stack

- **controller.php** — 1,000-line file handling all AJAX, Maps, MySQL & Shopify
- Raw PHP, no framework, no standards, credentials in plain text
- HTTP-triggered "crons" — if no caller, nothing runs
- Google Sheets as pricing source of truth, zero schema enforcement
- ~$4,000/month Maps API — every lookup recalculated fresh
- SFTP deploys → no rollback → no staging → no tests

Django tomorrow — the clean stack

- **Django 5.x + DRF** — framework-enforced separation of concerns
- Celery + Redis — background jobs run on schedule, always, automatically
- Redis caching for Google Maps — estimated 60–70% API cost reduction
- GitHub Actions CI/CD → every deploy tested, versioned, reversible
- Structured logging, sync dashboards, Sentry error tracking throughout
- Method CRM fully removed — 15 files gone, zero dependencies

YOUR ENGAGEMENT

5 migration phases — nothing goes dark

1 Foundation & Infrastructure

WEEKS 1–3

Stand up the Django project and eliminate critical security exposures before anything else. Produces a working, deployable skeleton with a clean CI/CD pipeline and staging environment — the foundation everything builds on.

- Django 5.x + Python 3.12
- DRF + Celery + Redis + PostgreSQL
- GitHub Actions CI/CD
- Staging environment
- Remove adminer.php + phpinfo.php
- Secrets → environment variables
- CORS lockdown
- MySQL → PostgreSQL migration script
- Sentry error tracking setup

2 Pricing Sync Engine

WEEKS 3–9

Rebuild the pricing sync pipeline from scratch. Replaces fragile HTTP-triggered crons with Celery Beat scheduled tasks that run automatically — no external caller required. All 6 sync types implemented, tested, and monitored.

- Django models: Product, Location, ZipCode, SyncQueue, SyncLog
- Google Sheets integration
- Price calculation service (clean + tested)
- Celery Beat scheduled tasks
- All 6 sync types
- Admin dashboard: sync status, queue depth, error logs

3 Checkout & Pricing API

WEEKS 6–9

Replace controller.php with a clean Django REST API. ZIP → geocode → nearest depot → pricing, fully cached with Redis. This is where the API cost reduction happens. Frontend swap is a single-line URL change — same UX, completely clean backend.

- DRF API: ZIP → geocode → depot → pricing
- Redis caching for Google Maps responses
- Shopify Draft Order via GraphQL
- Frontend endpoint swap
- Rate limiting + error handling + monitoring

4 Order Processing & Method CRM Removal

WEEKS 8–11

Replace Shopify webhook handling and permanently remove all Method CRM SOAP code. Django handles order creation, inventory deduction, and Google Sheets quantity updates automatically. 15 nusoap files deleted for good.

- Shopify webhook handler
- Inventory management in Django
- Google Sheets quantity updates (automated)
- Complete Method CRM removal (15 files)
- Order audit trail + payment status tracking

→ Removing Method CRM and rebuilding order processing in Django creates a clean, API-ready foundation that will significantly simplify a future HubSpot integration — which we'll scope as a separate engagement when Container One is ready.

5 Cutover & Decommission

WEEKS 11–14

Run PHP and Django in parallel, compare outputs, validate data integrity, then cut over cleanly. PHP decommissioned. You receive full documentation, a QA test suite, and a knowledge transfer session.

- Parallel run testing
- Full QA test suite
- Data verification
- Production DNS cutover
- PHP decommission
- Documentation + knowledge transfer

YOUR INVESTMENT & TIMELINE

$22,300 USD — billed phase by phase

YOUR TIMELINE — 14-16 WEEKS, PHASES OVERLAP BY DESIGN

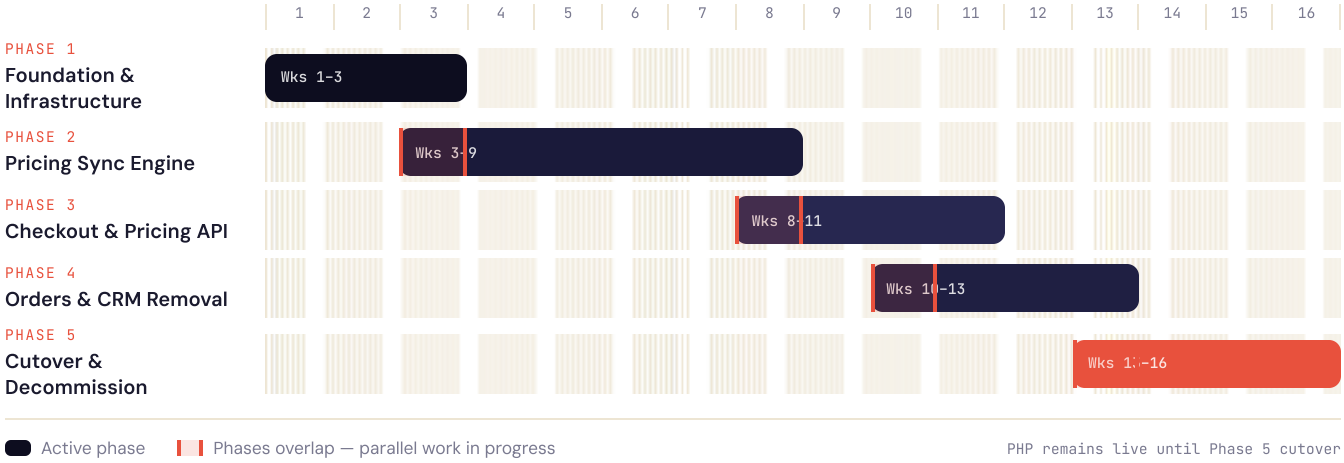

PHASE	WHAT YOU'RE GETTING	TIMELINE	YOUR INVESTMENT
Phase 1	Foundation & Infrastructure	Weeks 1–3	**$3,000**
Phase 2	Pricing Sync Engine	Weeks 3–9	**$5,600**
Phase 3	Checkout & Pricing API	Weeks 8–11	**$5,900**
Phase 4	Order Processing & Method CRM Removal	Weeks 10–13	**$4,300**
Phase 5	Cutover & Decommission	Weeks 13–16	**$3,500**
Your Total			**$22,300 USD**

PAYMENT SCHEDULE

Each phase is invoiced at kickoff. **Payment is due before each phase begins.** Phase 1 is due on signing. Gives you a natural gate to review work before the next commitment.

Want to move faster? No hard blockers prevent acceleration — reach out to discuss condensed delivery.

WHAT'S OUT OF SCOPE

- The ~$3k monkey patch (separate, in progress)
- HubSpot ↔ Shopify sync (future engagement)
- Shopify theme or frontend redesign
- Sheets → HubSpot pricing migration
- New product types during migration

CHANGE ORDERS

Work outside these 5 phases requires a written Change Order signed by both parties **before work begins.**

Verbal requests, Slack, or email do not constitute approval.

POST-MIGRATION

Monitoring & Dev Support

Monitoring & Dev Support

OPTIONAL · MONTHLY · CANCEL WITH 30 DAYS NOTICE

$999/mo

MONITORING + ALERTING + 10 DEV HRS/MO

ALWAYS-ON — MONITORING

- → Uptime monitoring + alerting — we know before you do
- → Sentry error tracking — real-time exception visibility across the Django stack
- → Sync pipeline health checks — queue depth, last run, failure alerts
- → Deployment verification — every CI/CD push confirmed clean
- → Monthly system health summary delivered to your team

MONTHLY DEV ALLOWANCE — 10 HOURS

- → Django bug fixes and minor changes
- → Shopify API & webhook issues related to the migration scope
- → Sync pipeline adjustments and monitoring tuning
- → Unused hours do not roll over month-to-month
- → Additional hours at $150/hr, billed monthly — or ask about discounted dev hour packages

NOT COVERED UNDER THIS SLA

- × Net-new features or scope changes (→ Change Order)
- × Shopify theme or storefront work
- × General Shopify store management
- × HubSpot or third-party integrations (→ separate engagement)

RESPONSE & RESOLUTION SLA

Support is delivered during business hours. All targets below apply on business days.

PRIORITY	DEFINITION	ACKNOWLEDGMENT	TARGET RESOLUTION
P1 — CRITICAL	System down, data loss, sync completely stopped	8 business hours	Next business day
P2 — HIGH	Degraded performance, intermittent failures, partial sync issues	Next business day	48 business hours
P3 — NORMAL	Minor issues, questions, small changes, non-urgent requests	3 business days	5 business days

HOW IT WORKS

This add-on activates at the end of Phase 5 — after cutover and handoff. Autonomous monitors the Django stack on your infrastructure and keeps you informed before issues become outages. Your plan includes **10 hours of development support per month** for bug fixes and changes related to the migration scope; additional hours are available at $150/hr. The first month is invoiced upon signing of a separate SLA agreement. Either party may cancel with 30 days' written notice. **The SLA covers what we built. Anything new is a Change Order.**

ALL-IN MONTHLY

$999/mo

Monitoring · alerting · 10 dev hrs
30-day cancellation

TERMS & CONDITIONS

What you need to know

INTELLECTUAL PROPERTY

Everything built becomes yours upon receipt of each phase payment. Full access handed off at each milestone — all code, configs, and documentation. No strings attached.

CHANGE ORDERS

Work outside this SoW requires a written Change Order signed by both parties before commencement. Verbal requests, Slack messages, or emails do not constitute approval. No exceptions.

CLIENT RESPONSIBILITIES

Timely access to credentials, environments, and Google Sheets is required. Delays in providing access may extend the phase timeline at no additional charge.

MONITORING & SUPPORT ADD-ON

If the Monitoring & Dev Support add-on is elected, Autonomous monitors the Django stack on Container One's infrastructure. Cloud hosting and infrastructure costs remain Container One's responsibility and are not included in the SLA fee.

PERFORMANCE ESTIMATES

API cost reduction estimates (60–70%) are based on expected cache hit rates and are not guaranteed. Actual savings depend on traffic patterns outside Autonomous's control.

VALIDITY

This agreement is valid for 30 days from the date on the cover. Pricing is subject to change after expiry. Phase 1 begins upon receipt of signed SoW and Phase 1 payment.

READY TO GET STARTED?

Sign below and Phase 1 kicks off immediately

Return this signed agreement with your Phase 1 payment and we'll begin foundation setup and security fixes in the first week. Your current system stays live throughout the entire migration. Questions before signing? hello@autonomoustech.ca

SIGNATURES

CONTAINER ONE — CLIENT

Glenn Taylor

Owner, Container One

Date: _____

AUTONOMOUS TECHNOLOGY INC.

Rizwan Qaiser

Autonomous Technology Inc.

Date: _____
